| ID | | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1 | | **Seward Mitigation Plan** | **400 days** | **Tue 11/25/08** | **Tue 06/08/10** |
| 2 | | **Review and Revise KPB 14.40 Roads** | **115 days** | **Tue 11/25/08** | **Tue 05/05/09** |
| 3 | | Develop Propose :Roads in Hazard Zone to withstand re occurring inundation, and convey water flow | 10 days | Tue 11/25/08 | Mon 12/08/08 |
| 4 | | Pre Ordinance work (RSAB, Engineering& Legal) | 30 days | Tue 12/09/08 | Mon 01/19/09 |
| 5 | | RSAB Meeting introduction | 0 days | Mon 01/12/09 | Mon 01/12/09 |
| 6 | | SBCFSA Meeting | 0 days | Mon 02/02/09 | Mon 02/02/09 |
| 7 | | RSAB Work Session | 0 days | Mon 02/09/09 | Mon 02/09/09 |
| 8 | | RSAB action | 0 days | Tue 03/10/09 | Tue 03/10/09 |
| 9 | | SBCFSA Meeting | 0 days | Mon 04/06/09 | Mon 04/06/09 |
| 10 | | Packet Deadline | 0 days | Mon 04/06/09 | Mon 04/06/09 |
| 11 | | Ordinance Introduction to revise Hazard Road Standard | 0 days | Tue 04/07/09 | Tue 04/07/09 |
| 12 | | Public Hearing on Ordinance | 0 days | Tue 04/21/09 | Tue 04/21/09 |
| 13 | | Public Hearing / Action on Ordinance (in Seward) | 0 days | Tue 05/05/09 | Tue 05/05/09 |
| 14 | | **Review and Revise KPB 20 Subdivisions (20.20.260 20.20.030 Location)** | **65 days** | **Tue 05/05/09** | **Tue 08/04/09** |
| 15 | | Develop Propose :Roads layout to convey water flow and provide egress during flood event | 10 days | Tue 05/05/09 | Mon 05/18/09 |
| 16 | | Develop Alternate Purpose not to locate residential in High Hazard Areas | 5 days | Tue 05/19/09 | Mon 05/25/09 |
| 17 | | Pre Ordinance work (Planning, SBCFSAB & Legal) | 30 days | Tue 05/26/09 | Mon 07/06/09 |
| 18 | | Planning Meeting introduction | 0 days | Mon 05/11/09 | Mon 05/11/09 |
| 19 | | SBCFSA Meeting | 0 days | Mon 05/18/09 | Mon 05/18/09 |
| 20 | | Planning Work Session | 0 days | Tue 05/26/09 | Tue 05/26/09 |
| 21 | | Planning action | 0 days | Mon 06/08/09 | Mon 06/08/09 |
| 22 | | SBCFSA Meeting | 0 days | Mon 06/01/09 | Mon 06/01/09 |
| 23 | | Packet Deadline | 0 days | Mon 06/01/09 | Mon 06/01/09 |
| 24 | | Ordinance Introduction to revise Hazard Planning | 0 days | Tue 06/16/09 | Tue 06/16/09 |
| 25 | | Public Hearing on Ordinance | 0 days | Tue 07/07/09 | Tue 07/07/09 |
| 26 | | Public Hearing / Action on Ordinance | 0 days | Tue 08/04/09 | Tue 08/04/09 |
| 27 | | **Review and Revise KPB 21.06 or add Alternate section to address Gravel Hazard Areas** | **130 days** | **Tue 08/04/09** | **Tue 02/02/10** |
| 28 | | Develop Propose :Protect Life & Safety | 10 days | Tue 08/04/09 | Mon 08/17/09 |
| 29 | | Develop Alternate Purpose: Minimize Public & Private Loss | 10 days | Tue 08/18/09 | Mon 08/31/09 |
| 30 | | Pre Ordinance work (KRC, SBCFSAB & Legal) | 30 days | Tue 09/01/09 | Mon 10/12/09 |
| 31 | | SBCFSAB Meeting introduction | 0 days | Mon 10/19/09 | Mon 10/19/09 |
| 32 | | Planning Meeting Introduction | 0 days | Mon 10/26/09 | Mon 10/26/09 |
| 33 | | KRC Staff Meeting | 0 days | Mon 11/02/09 | Mon 11/02/09 |
| 34 | | Planning Work Session | 0 days | Mon 11/09/09 | Mon 11/09/09 |
| 35 | | Planning action | 0 days | Mon 11/23/09 | Mon 11/23/09 |
| 36 | | SBCFSA Work Session | 0 days | Mon 11/16/09 | Mon 11/16/09 |
| 37 | | SBCFSAB Action | 0 days | Mon 12/07/09 | Mon 12/07/09 |
| 38 | | Packet Deadline | 0 days | Mon 12/21/09 | Mon 12/21/09 |
| 39 | | Ordinance Introduction to revise Hazard Planning | 0 days | Tue 01/05/10 | Tue 01/05/10 |
| 40 | | Public Hearing on Ordinance | 0 days | Tue 01/19/10 | Tue 01/19/10 |
| 41 | | Public Hearing / Action on Ordinance | 0 days | Tue 02/02/10 | Tue 02/02/10 |
| 42 | | **2009 Lidar Data** | **43 days** | **Thu 10/15/09** | **Tue 12/15/09** |
| 43 | | Fly Lidar | 22 days | Thu 10/15/09 | Fri 11/13/09 |
| 44 | | Data Available | 0 days | Tue 12/15/09 | Tue 12/15/09 |
| 45 | | **Identify and Develop "Safe Zones"** | **60 days** | **Mon 12/21/09** | **Fri 03/12/10** |
| 46 | | Hydrologist Recommendation | 30 days | Mon 12/21/09 | Fri 01/29/10 |
| 47 | | Planning & Land Management Evaluation & Recommendation | 30 days | Mon 02/01/10 | Fri 03/12/10 |
| 48 | | **TSUNAMI INUNDATION MAPPING FOR ALASKA COASTAL COMMUNITIES** | **0 days** | **Tue 06/30/09** | **Tue 06/30/09** |
| 49 | | Report Released for Seward | 0 days | Tue 06/30/09 | Tue 06/30/09 |
| 50 | | **FIRM Maps (FEMA)** | **186 days** | **Mon 06/15/09** | **Tue 03/02/10** |
| 51 | | Mapping Complete | 0 days | Mon 06/15/09 | Mon 06/15/09 |
| 52 | | Draft Letter & Identify impacted Properties | 4 wks | Mon 07/06/09 | Fri 07/31/09 |
| 53 | | SBCFSAB Review | 0 days | Mon 08/03/09 | Mon 08/03/09 |
| 54 | | 90 Day Comment | 90 days | Mon 08/03/09 | Fri 12/04/09 |
| 55 | | Revise per Comments | 10 days | Mon 12/07/09 | Fri 12/18/09 |
| 56 | | SBCFSAB Review | 0 days | Mon 12/21/09 | Mon 12/21/09 |
| 57 | | Write Ordinance | 14 days | Mon 12/21/09 | Thu 01/07/10 |
| 58 | | Packet Deadline | 0 days | Mon 01/18/10 | Mon 01/18/10 |
| 59 | | Introduce Ordinance to Adopt FIRM Map | 0 days | Tue 02/02/10 | Tue 02/02/10 |
| 60 | | Public Hearing on Ordinance | 0 days | Tue 02/16/10 | Tue 02/16/10 |
| 61 | | Public Hearing / Action on Ordinance | 0 days | Tue 03/02/10 | Tue 03/02/10 |
| 62 | | **Define Hazard Area And Evaluate Differential Tax Zones for enhanced level of service** | **121 days** | **Mon 12/21/09** | **Tue 06/08/10** |
| 63 | | Develop Purpose :Protect Life & Safety | 10 days | Mon 12/21/09 | Fri 01/01/10 |
| 64 | | Develop Alternate Purpose: Minimize Public & Private Loss | 10 days | Mon 01/04/10 | Fri 01/15/10 |
| 65 | | Pre Ordinance work (KRC, SBCFSAB & Legal) | 30 days | Mon 01/18/10 | Fri 02/26/10 |
| 66 | | SBCFSAB Meeting introduction | 0 days | Mon 03/01/10 | Mon 03/01/10 |
| 67 | | Planning Meeting Introduction | 0 days | Mon 03/08/10 | Mon 03/08/10 |
| 68 | | KRC Staff Meeting | 0 days | Mon 03/15/10 | Mon 03/15/10 |
| 69 | | Planning Work Session | 0 days | Mon 03/22/10 | Mon 03/22/10 |
| 70 | | Planning action | 0 days | Mon 04/12/10 | Mon 04/12/10 |
| 71 | | SBCFSA Work Session | 0 days | Mon 04/05/10 | Mon 04/05/10 |
| 72 | | BCFSAB Action | 0 days | Mon 04/19/10 | Mon 04/19/10 |
| 73 | | Packet Deadline | 0 days | Mon 04/19/10 | Mon 04/19/10 |
| 74 | | Ordinance Introduction to revise Hazard Planning (in Seward) | 0 days | Tue 05/04/10 | Tue 05/04/10 |
| 75 | | Public Hearing on Ordinance | 0 days | Tue 05/18/10 | Tue 05/18/10 |
| 76 | | Public Hearing / Action on Ordinance | 0 days | Tue 06/08/10 | Tue 06/08/10 |

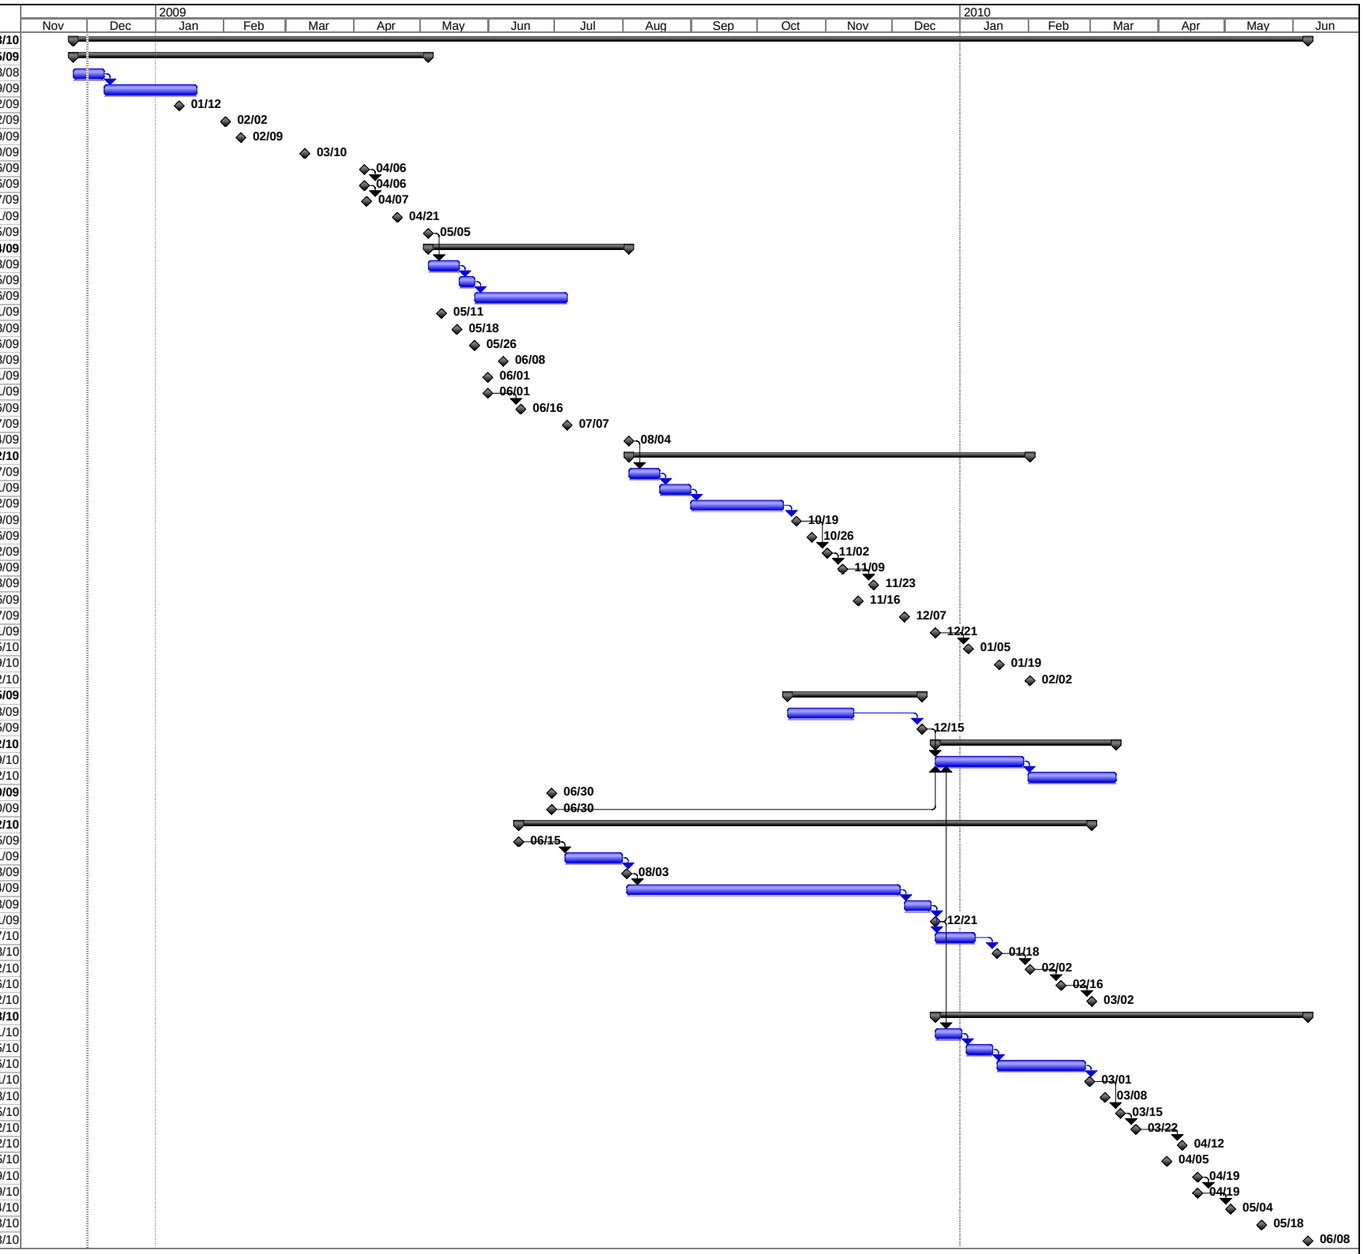


Project: Project Summary
Date: Mon 12/01/08

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
